



GRAPEVINE – COLLEYVILLE ISD 2016 BOND PROJECT UPDATE

February 24, 2020

Huckabee
MORE THAN ARCHITECTS



SUMMER 2019 RENOVATIONS

Huckabee
MORE THAN ARCHITECTS

GRAPEVINE HIGH SCHOOL



- + Front entry/controlled vestibule and attendance area are finished
- + Demo/Refresh will begin on the existing and vacated administrative areas
- + Tracking smoke dampers for replacement over the stage, tentatively scheduled for Spring Break
- + Replace stage flooring during Spring Break
- + Installation of the fire suppression resumes in June along with replacing the floor in Gym 1



GRAPEVINE HIGH SCHOOL



GRAPEVINE HIGH SCHOOL



GRAPEVINE ELEMENTARY SCHOOL

NEW CLASSROOM ADDITION




- + Brick veneer is being completed this next week
- + All overhead and finish out of devices are being completed
- + Millwork has arrived and is being installed
- + Flooring will begin at the end of this month



GRAPEVINE ELEMENTARY SCHOOL

NEW CLASSROOM ADDITION

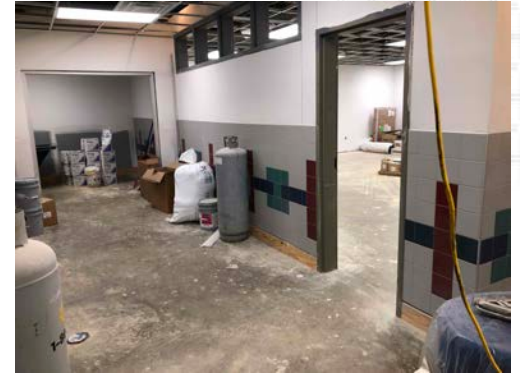

GLENHOPE ELEMENTARY SCHOOL

REMEDIATION AT EXTERIOR



- + Replacement of exterior wall at the classroom addition to take place Summer 2020



Huckabee

SUMMER 2020 RENOVATIONS

2020 PROJECTS

+ Swim Center

- Pre proposal held 02.18.20 with sub consultants
- Proposal due 03.05.20
- Board Meeting to approve 03.23.20
- Construction to start in May 2020

+ CHHS, BCES, HES, BES, CES

- All Sign 03.12.20
- Receive proposals 04.19.20
- Board Meeting to approve 04.27.20
- Construction to start in June 2020

+ Administration Building

- Selected GC brought to Board for approval 03.23.20
- Staff recommending both alternates
- Interiors and Courtyard to start 06.01.20

+ CTMS Creek

- Civil Engineer completed Phase 1 analysis and provided District with Phase 2 proposal for survey and engineering
- Geotechnical testing needed as part of Phase 2



Huckabee

MORE THAN ARCHITECTS
